PENTUCKET

Building Committee Meeting

May 12, 2020










May 12, 2020

•	Project Schedule	Discuss
•	Permit update	Discuss
•	Interiors Subcommittee update	Discuss
•	ERP Status	Discuss

Schedule





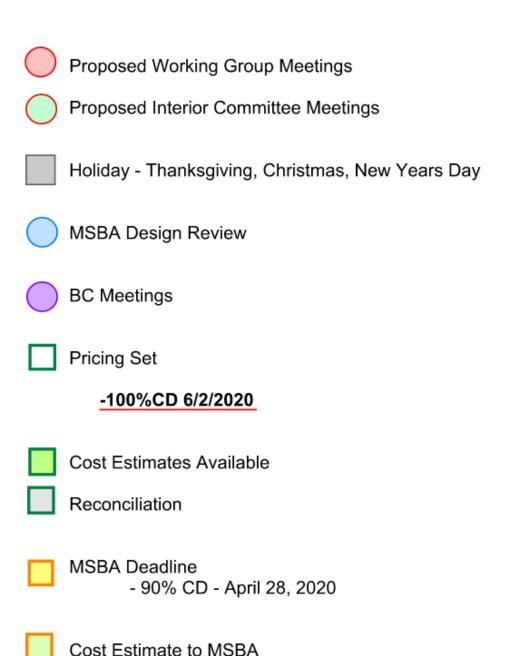

MSBA Schedule Update

90% CD

✓ March 31

April 28, 2020

TBD

June 2, 2020

Pricing Set

90%CD Submission to MSBA

Waiting for MSBA's 90%CD comments

Bid Set



Permitting Update

✓	Tues. Oct. 15	West Newbury Planning Board Meeting/Review Dover Amendment criteria
✓	Wed. Oct 30	Neighborhood Meeting at 7:30p
✓	Wed. Oct 30	Submit Complete Site Plan Review Application and Plans to Groveland and West Newbury
✓	Wed. Nov 6	Pre-Application Conference with West Newbury Planning Board
✓	Tues. Dec 17	West Newbury Planning Board Site Plan Review Public Hearing
✓	January 20, 2020	Meridian Peer Review –Responses Meeting
✓	February 4, 2020	W. Newbury Planning Board Site Plan Review Public Hearing Continues
/	March 4, 2020	W. Newbury Planning Board Certificate of Vote signed.



May 19, 2020 Groveland Planning Board Public Hearing Continues



✓ Friday Oct. 18, 2019 Pentucket Site Walk-through with West Newbury ConCom

✓ Saturday, Oct. 26, 2019 Pentucket Site Walk-through with Groveland ConCom

✓ November 4, 2019 ConCom Notices of Intent – NOI

✓ November 18, 2019 West Newbury ConCom Meeting

✓ December 11, 2019 Groveland ConCom Meeting

April 22, 2020

✓ January 20, 2020 Meridian Peer Review —Responses Meeting

✓ February 3, 2020 West Newbury ConCom Meeting Continuation

✓ February 24, 2020 West Newbury ConCom Meeting Continuation

April 16, 2020 West Newbury ConCom Meeting Continuation, (Received Contingent approval)

D+W/NE Provided Revised documents
(Waiting for OOC)

May 13, 2020 Groveland ConCom Meeting Continuation

Permitting Update

Plumbing Variance: 50 % reduction of plumbing fixture count at the Stadium.

November 18, 2019 Submitted variance to State Plumbing Board

✓ November 25, 2019 <u>Variance Granted</u>

Structure Variance: Request to reduce fire resistance rating for Primary Structural from above 20' from 1hr. to 0 hr.

November 20, 2019 Submitted variance to the West Newbury Building Inspector

December 18, 2019 Submitted variance to the *new* West Newbury Building Inspector

January 27, 2020 Received Inspector letter for State submission

March 10, 2020 Received Inspector denial letter for State Submission

March 11, 2020 Served variance application to the WN Inspector and State

"Check back on May 18" - Patty Barry, 05-06-2020 email

MAAB Variance: Allow grading of existing path to remain with minor upgrades

April 15, 2020 Served variance application WN ADA coordinator, WN Building Inspector,

Northeast Independent Living Program and MAAB.

"Potential meeting on May 11"








Interiors Sub-Committee Update



Building Parti

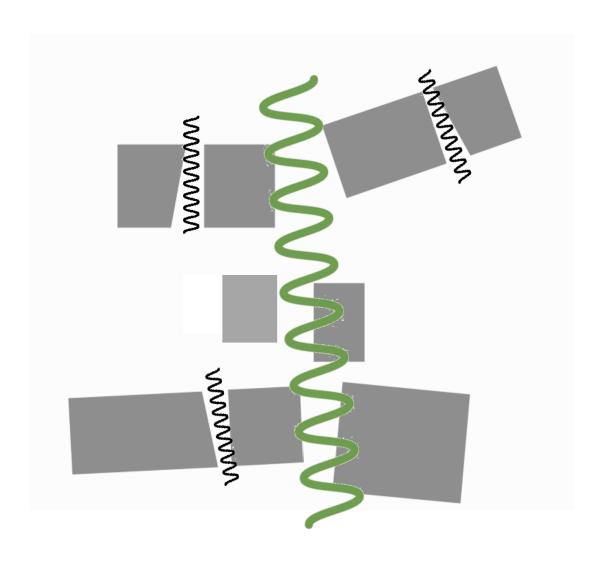

"A series of buildings woven together by a common thread. The thread becomes the key element, interlacing the buildings, symbolizing the connections between the three towns, joining as one building. The connection points, or thread, are the areas in the building where students, faculty and community can gather. The Extended Learning areas and Café nooks are part of these spaces."

Exterior Palette of Materials











Interior Palette of Materials

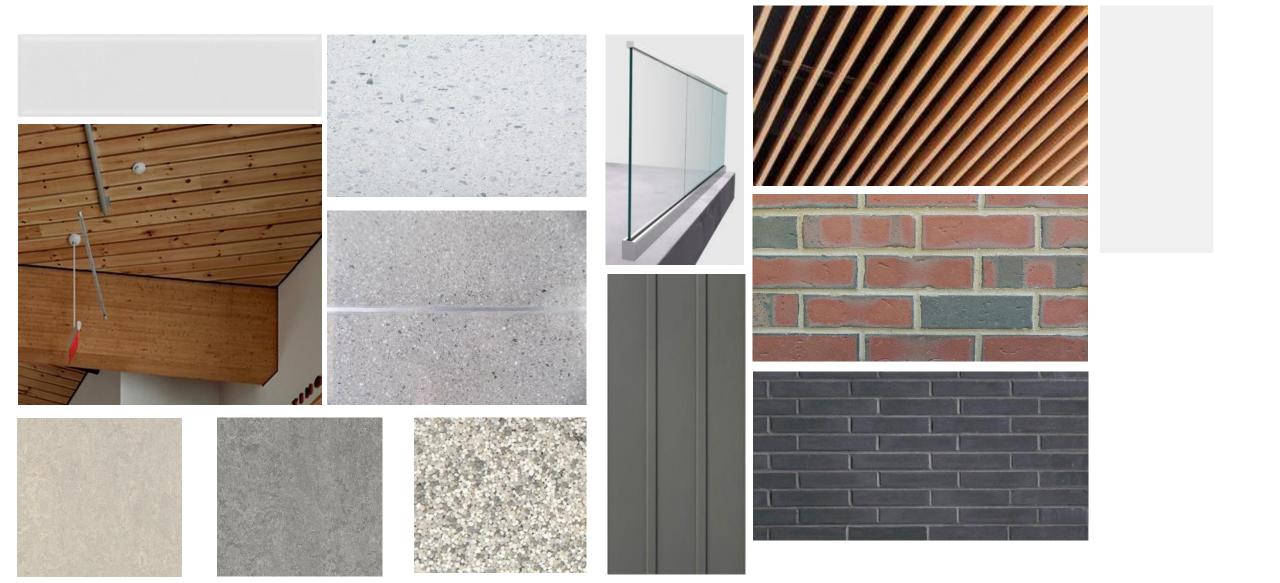


Building Floor Plans



1st Floor

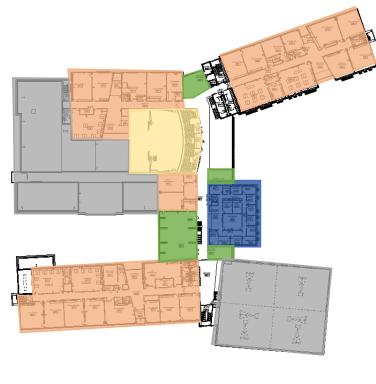

2nd Floor

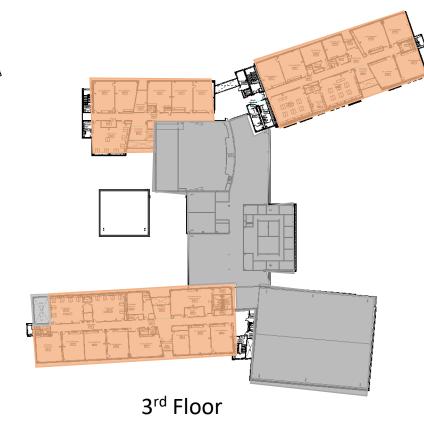

November 21, 2019

Student Dining & Library

January 2, 2020

Academic - Classrooms, Corridors, Extended Learning

January 16, 2020

Review Updates to Corridor & Extended Learning, Student Dining & Upper Café Wall

January 30, 2020

Athletic – Gymnasium, Locker Rooms, Health

Art, Music & Auditorium

February 27, 2020


Administration, Guidance & Support Spaces, toilets

April 30, 2020


Wrap up


Color Theory & Wayfinding





Palette A

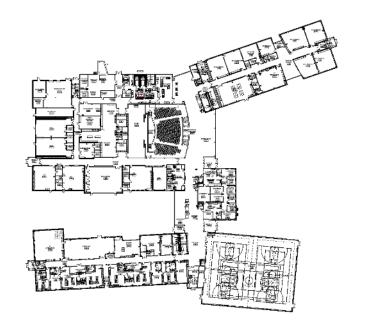

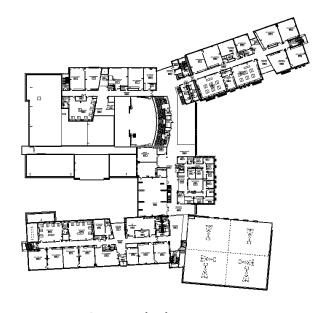




First Floor Second Floor Third Floor





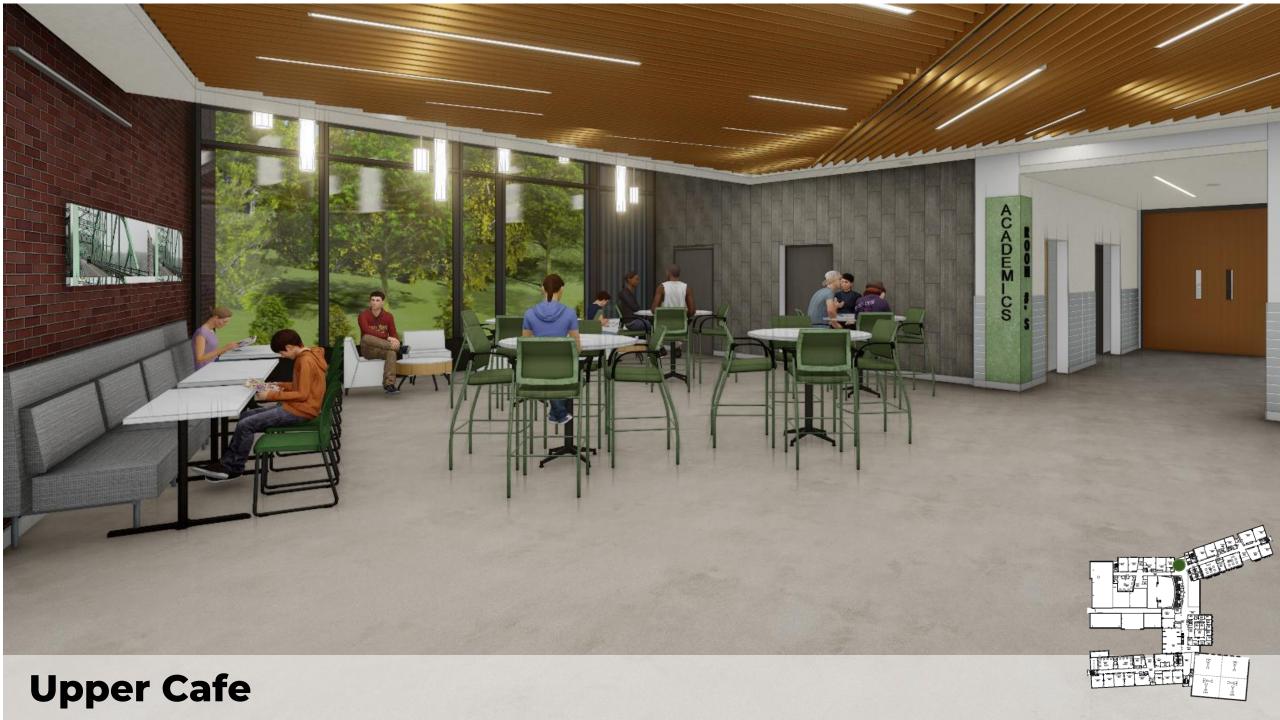

































ERP 01 Status

Scope of Work	Budget approved 04/09	Buyout complete 05/12
Abatement & Demolition	\$3,250,000	\$3,250,000
Site Work*	\$15,450,000	\$14,900,000
Concrete	\$4,900,000	\$4,750,000
Structural Steel	\$5,100,000	\$5,106,000
Glulam	\$789,000	\$725,000
Ground Improvement	\$1,499,000	\$1,499,000
Temp Boiler and DHW	\$492,270	\$492,700
Allowances	\$172,000	\$232,000
TOTAL	\$31,626,270	\$30,954,700

^{*}Note – Saving shown in Sitework are the result of moving guardrail and landscape curbing out of the ERP scope and into the remaining CD90 estimate scope.

Thank you!



